

To: CVG Airlines and Tenants

Subject: Updated Expansion Joint Project Estimated Schedule

Date: 11/29/2022


Construction continues for the replacement of expansion joints in Concourse B and the AGT, as well as begins in Concourse A this week. The schedule has been updated since previous communication.

Work will now continue through approximately December 5th, 2022 and will cease until the beginning of 2023 due to product availability. Updated scheduling for continued work will be sent once the schedule for 2023 is finalized.


Please note that this order is subject to change as operational impact may necessitate.

Work occurring now through end of the year:

Gate B16 threshold from 8:00 AM Tuesday, November 29th to the evening of Thursday, December 1st. B16 will be closed during this time.




The west end of the tunnel has barricades up and work will be completed by the end of this week (Friday, December 2nd)





Work will begin on the expansion joints in Concourse A near the Starbucks location and Over the Rhine shop on Tuesday, November 29th. This will not have an operational impact on any gates. Barriers will be in place with signage to help redirect passengers around them.

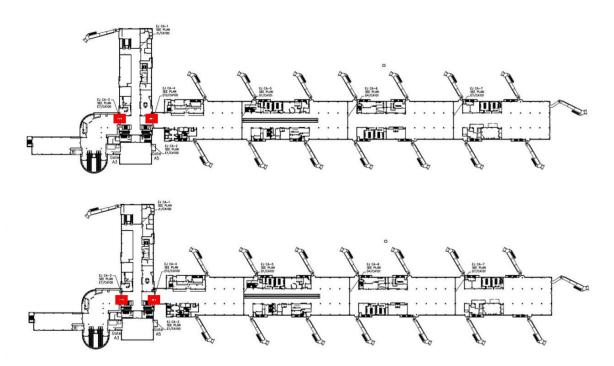

All other expansion joints that have not been replaced will be completed after the beginning of 2023.

Any gates affected by each phase will be communicated and coordinated with airline carriers.

Should you have any questions regarding the work, please contact JW Lucas at jlucas@cvgairport.com or 859-743-5861

Thank you for your cooperation.

OM2022-13.2 Page **2** of **2**
