

To: CVG Airlines and Tenants
Subject: Terminal Escalator Modifications
Date: January 28, 2021

EFFECTIVE FEBRUARY 1st, 2021

Beginning Monday, February 1st, 2021, the escalators in the Terminal will begin a series of repairs and installations throughout the year. The work is currently set to be finished at the beginning of November 2021. Below is the current schedule of work, which may be subject to change:

ID	Task Name	Duration	Start	Finish
0	Escalator Mods	200 days	Mon 2/1/21	Fri 11/5/21
1	3-9A Installation	11 wks	Mon 2/1/21	Fri 4/16/21
2	3-9B Major Repair	6 wks	Mon 2/15/21	Fri 3/26/21
3	3-9C Major Repair	6 wks	Mon 5/3/21	Fri 6/11/21
4	3-9D Installation	11 wks	Mon 4/19/21	Fri 7/2/21
5	3-2C Installation	18 wks	Mon 7/5/21	Fri 11/5/21
6	3-2D Installation	18 wks	Mon 7/5/21	Fri 11/5/21

Some of the work necessary for these modifications involves welding and grinding, which will produce additional noise, bright light, and smoke. To aid in some of this, barriers will be placed throughout the Terminal as shown in the images below. Additionally, signage will be put on the barricade walls on each level to help redirect traffic to use other escalators.


Ticketing Level Barricade:



Baggage Claim Level Barricade:



AGT Level Barricade:

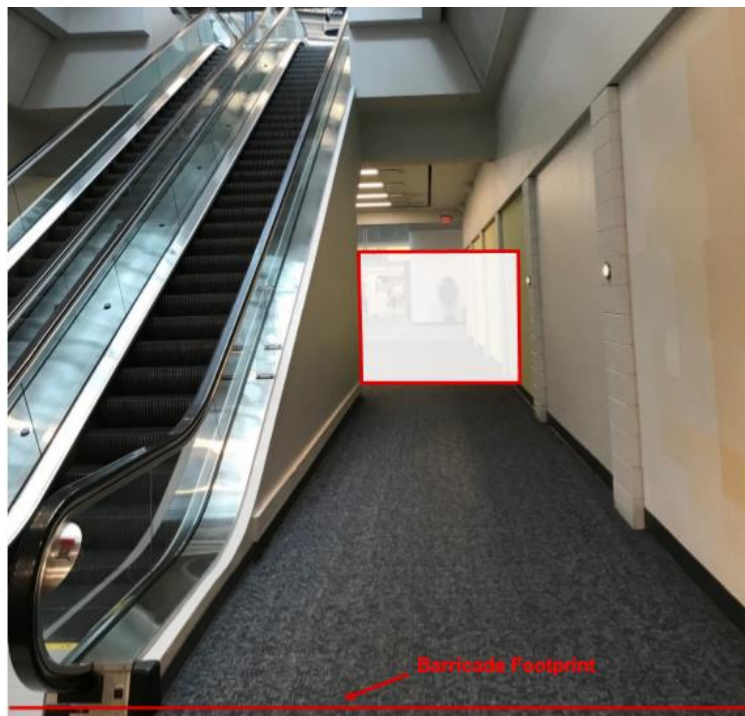

To help mitigate surprise of any additional noise in the Terminal, it has been requested that the Terminal Services team be notified of any welding and grinding prior to the day of work. Once notified, the necessary tenants will be provided with the information to help prepare those working during that period.

If you have any questions about the work being done, please contact Kevin Watts (kwatts@cvgairport.com).

Thank you for your cooperation.
