


## To: CVG Airlines and Tenants Subject: Concourse B Apron Rehabilitation Project Date: 9/30/2022

## **BEGINS MONDAY, October 3<sup>rd</sup>, 2022**

Beginning Monday, October 3<sup>rd</sup> at 7:00 AM, Harper Company will proceed with the Concourse B Apron Rehabilitation Project consisting of 10 phases. The work includes approximately 2.25 million square feet of pavement rehabilitation, including R2S & Ramp 3 areas and taxi lanes Golf & Romeo. Additionally, the work will include the demolition of 15 doghouses, new pavement markings, airfield signage and lighting work, airfield electrical demolition and installation, and storm drainage work. **The completion of all 10 phases of work is currently estimated to end on November 18, 2023.** Please note that the names of these phases do not correlate with the order in which they will occur.


Each phase scheduled consists of an average of 3 gates impacted, and an average of 33 days of work per each phase. The airport will work with the airlines and other stakeholders impacted by this work and will communicate on a scheduled basis prior to moving to each phase.

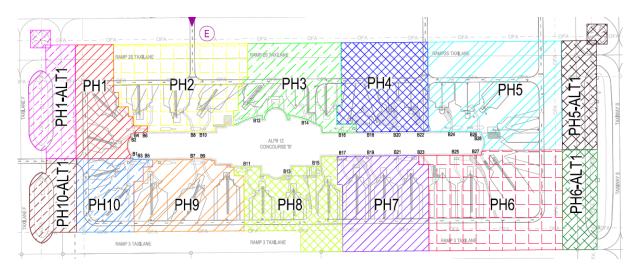

Please see an image of the (10) phase locations around Concourse B below:

The project will begin with Phase 7 which will occur at Gates B17, B19, and B21. The current dates for this phase are October 3, 2022 to November 11, 2022. It should be noted that the Vehicle Service Road (VSR) in this area will be closed during this time.

Please see detailed image of Phase 7 below:

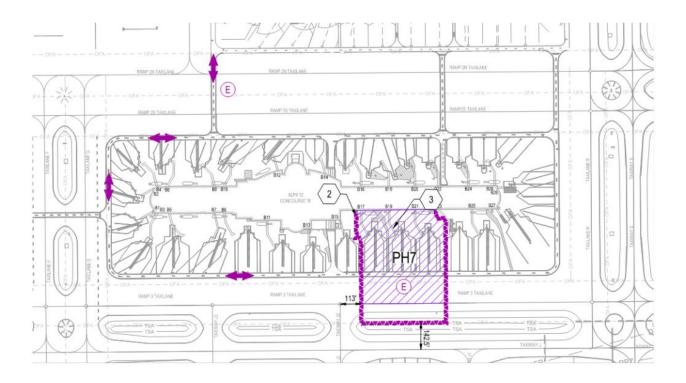

Additionally, you will find the most updated schedule based on the current timing of each phase below. *Please note that the schedule is subject to change per delays that may occur during each phase.* 

						Sch	edule	e Revision 09	/19/2	22
						DELTA		AMERICAN		PER PHASE COMMENTS
START	FINISH	Dave	Phase	Gates		Gates		Gates		PER PHASE COMMENTS
START	HINISH	Days	Plidse	Gales			1			Typical of the majority of the phases: The entire apron will
										be barricaded off, except as noted.
10/03/22	11/11/22	40	7	B17		3		0		Can light procurement issues caused phase 7 to proceed before 6.
				B19						
				B21						
11/12/22	12/22/22	45	6	B23		3		0		There is a concern for the shoulder work of this phase.
				B25						Asphalt this late in the season is vulnerable by the weather. There is a potential some work may be pushed to a future phase.
				B27						
				B12			]			2 Doghouse Demo Only. Reference attached drawing for
01/03/23	01/30/23	28	3	B16		0		1		the affected barricaded area. A refined area will remain
				B18					L F	barricaded until April. Some gate operations may be
				B4						1 Doghouse Demo Only. Reference attached drawing for
01/31/23	02/21/23	22	1&2			1		0		the affected barricaded area. A refined area will remain
				B6						barricaded until April. Some gate operations may be affected for daily operation or RON.
				<b>B6</b>			{			anected for daily operation of RON.
02/22/23	04/03/23	41	2	B8		0		0		
	21,00,20			B10		-				
				B12			1			
04/04/23	04/29/23	26	3	B14		0		0		
				B16						
				B18						
05/01/23	06/01/23	32	4	B20		0		3		
				B22			-			
06/02/23	07/10/23	39	5	B24 B26		0		3		Potential PBB B26
00/02/25	07/10/25	35		B26 B28		Ů		2		FULCILIOI PDD D20
				B20 B2					ŀ	
07/11/23	08/05/23	30	1	B4		2		0		Potential PBB B26
0.0 /0.0 /0.5	00 10 5 15 5			B1			1			D: 1000 000
08/10/23	09/15/23	37	10	B3		2		0		Potential PBB B26
09/16/23		33	9	B5		3		0		
	10/18/23			B7						
				B9						
10/19/23	11/16/23	29	8	B11		3		0		
				B13						
				B15						

For questions regarding the project, please see the following contacts:

Damian Weller (CVG Airport Authority) – 859-206-2044 or <u>dweller@cvgairport.com</u> JW Lucas (CVG Airport Authority) – 859-743-5861 or <u>jlucas@cvgairport.com</u>

Thank you for your cooperation
