



## Operations Memorandum

To: CVG Airlines and Tenants

Subject: Updated Expansion Joint Project Estimated Schedule

Date: 2/3/2022

**Please note that the dates and areas are subject to change as operational impact may necessitate.**


### Terminal

The third & final phase at the TSA Checkpoint is wrapping up and is scheduled to be complete by end of day February 8<sup>th</sup>.

The following locations on Ticketing level of the Terminal will begin the week of February 6<sup>th</sup>. The west end joint will begin work around 6:30 PM on Monday, February 6<sup>th</sup>. This work will take approximately 5 days to be completed and will only be worked on during evening & overnight hours as to minimize impact to departure traffic.


The east end joint will begin work after 8:30 PM on Wednesday, February 8<sup>th</sup>. This work will take approximately 5 days to be completed and will only be worked on during evening & overnight hours as to minimize impact to departure traffic.

Barriers will be in place at both locations, and signage will be set to help direct passengers around the barriers.

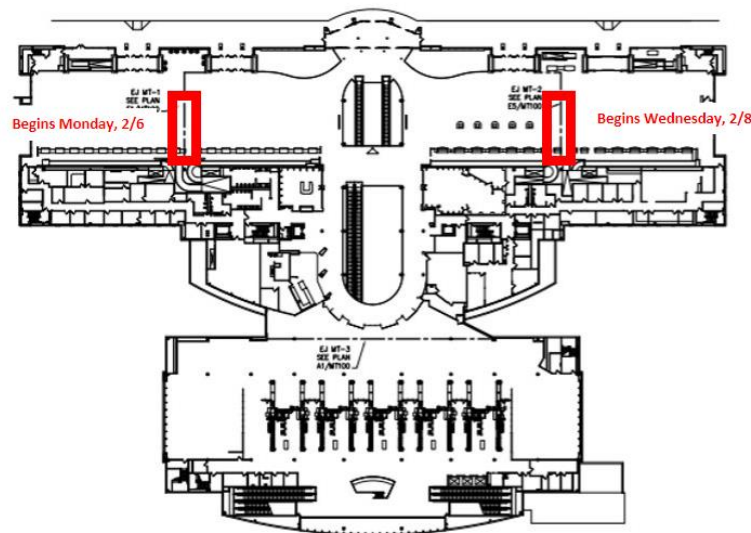

Once the initial 2/3 of the expansion joints on ticketing level are completed, the final 1/3 will be worked on during the week of 2/13. Similarly, these sections will take approximately 5 days to be completed and will only be worked on during evening and overnight hours as to minimize impact to departure traffic.

Barriers will be in place at both locations, and signage will be set to help direct passengers around the barriers.

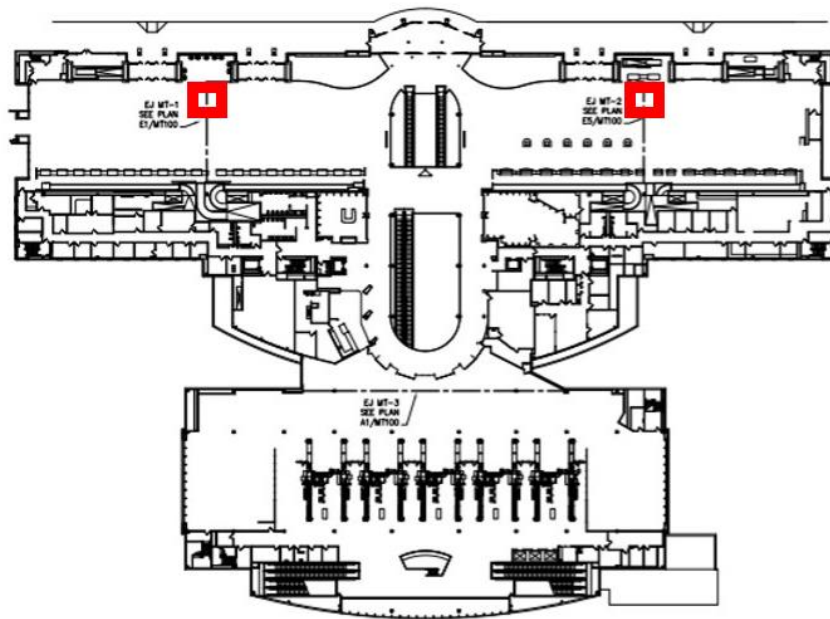

This is the final scheduled communication for this project, barring any updates relating to schedule or location.

Should you have any questions regarding the work, please contact JW Lucas at [jlucas@cvgairport.com](mailto:jlucas@cvgairport.com) or 859-743-586 or contact Tom Dorning at [tdorning@cvgairport.com](mailto:tdorning@cvgairport.com) or 859-655-5428.

Thank you for your cooperation.
