

Operations Memorandum

To: CVG Airlines and Tenants

Subject: Concourse B Apron Rehabilitation Project Phase 5

Date: 5/23/2023

Effective May 30, 2023


Beginning Tuesday, May 30th, *weather pending*, Harper Company will close out Phase 4 of the Concourse B Apron Rehabilitation Project, and transition into Phase 5 after the morning departure push. **This will reopen gates B18, B20, and B22, and close gates B24, B26, and B28. (note that B18 is prioritized to open first).** Ramp 2S Taxilane will be closed north of these gates to Taxiway S for the duration of this phase. Taxilane R will be closed from Gate B28 to Ramp 2N. Taxiway S will be closed north of Taxiway J to Ramp 2N. Ramp 3 will be closed from Taxilane R to Taxiway T.

The vehicle service road will be closed around Gates B24, B26, and B28.


The vehicle service road crossing of Ramp 2N and 2S will be closed at the east end of Concourse B, and markings will be removed.

The phase is currently scheduled to be completed on July 7th, 2023. Phase 5 will be conducted in two parts: Part A from 5/30/23 to 6/23/23 and Part B from 6/24/23 to 7/7/23. Please see image of Phase 5 Parts A and B below:

Part A:

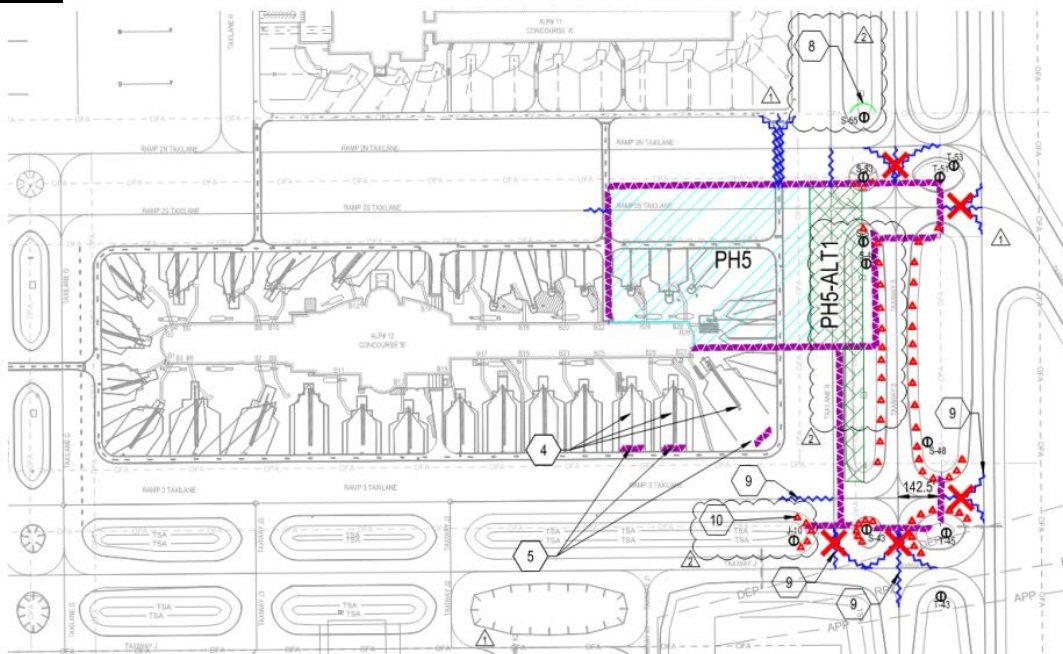


Part B:

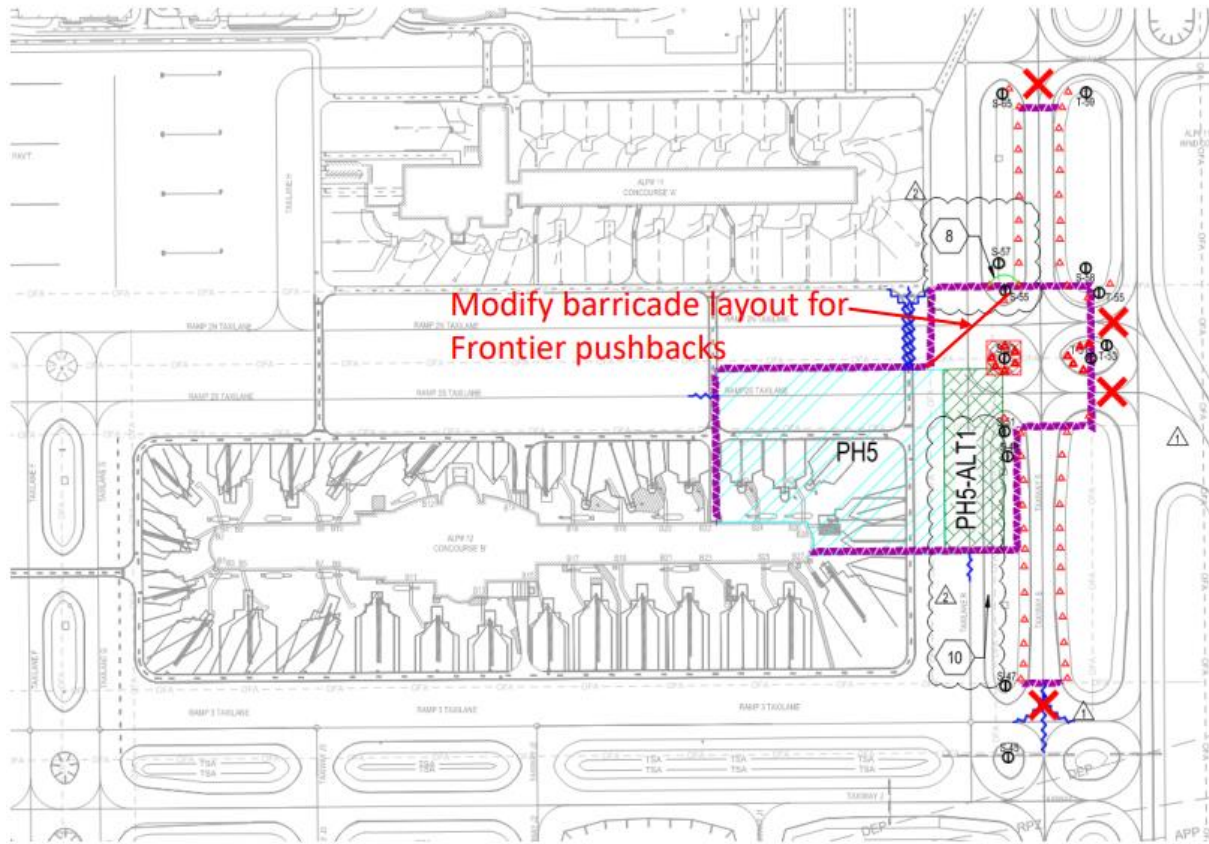

The work area will be surrounded by interlocking, low-profile barricades. ARFF routes will be provided with gaps in the barricade.

Pedestrians and vehicle traffic are to stay outside of the barricade during the closure. Additionally, you will find the most updated schedule based on the current timing of each phase below. ***Please note that the schedule is subject to change per delays that may occur during each phase.***

PHASE	START	FINISH	DAYS	GATE IMPACTS
7	10/03/22	11/15/22 Complete	43	B17, B19, B21 closed
6*	11/15/22	12/21/22 *Complete	45	B23, B25, B27 closed
2 Limited	01/03/23	01/31/23 Complete	29	B8, B10 available for RON
1 Limited	02/01/23	02/15/23 Complete	21	B8 closed; B4 & B6 open at night
2	02/20/23	03/31/23 Complete	40	B6, B8, B10 closed
3	03/31/23	04/27/23 Complete	26	B12, B14, B16 closed
4	04/28/23	05/30/23 (tentative)	31	B18, B20, B22 closed
5	05/30/23 (tentative)	07/7/23	36	B24, B26, B28 closed
1	07/??/23	08/04/23	34	B2, B4 closed
10	08/5/23	09/9/23	36	B1, B3 closed
9	09/10/23	10/13/23	34	B5, B7, B9 closed
8	10/15/23	11/11/23	29	B11, B13, B15 closed

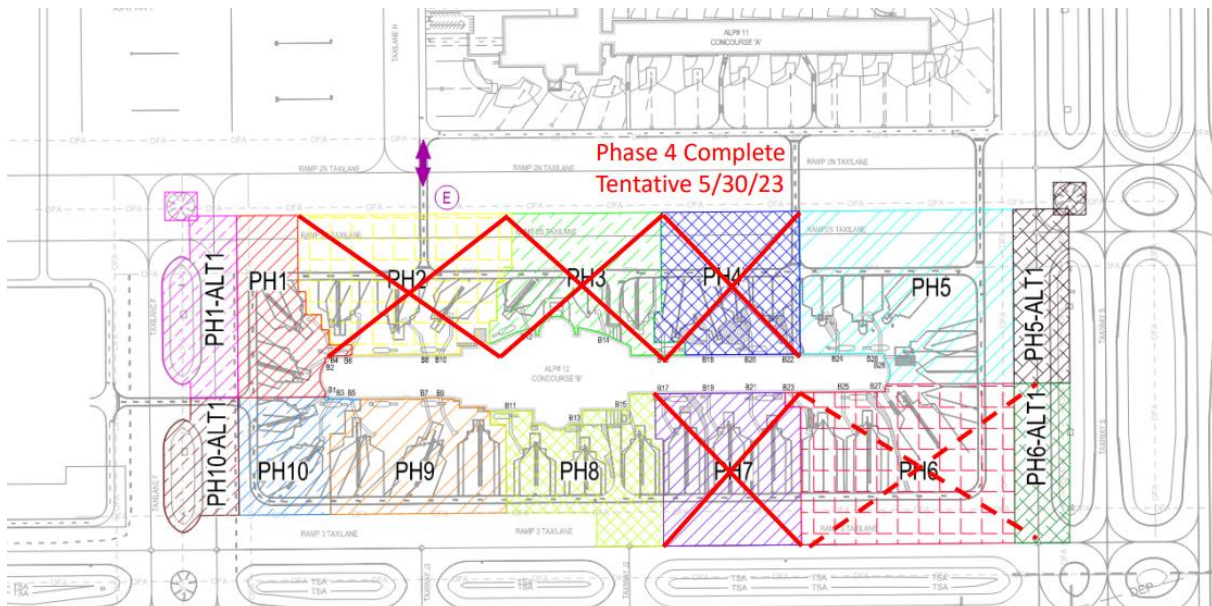

For questions regarding the project, please see the following contacts:

Damian Weller (CVG Airport Authority) – 859-206-2044 or dweller@cvgairport.com

JW Lucas (CVG Airport Authority) – 859-743-5861 or jucas@cvgairport.com
