

To: CVG Airlines and Tenants

Subject: Concourse B Apron Rehabilitation Project Phase 4

Date: 4/21/2023


Effective April 28, 2023


Beginning Friday, April 28th, *weather pending*, Harper Company will close out Phase 3 of the Concourse B Apron Rehabilitation Project, and transition into Phase 4. **This will reopen gates B12, B14, and B16, and close gates B18, B20, and B22.** Ramp 2S Taxilane will be closed north of these gates for the duration of this phase. In the near future, Ramp 2S and 2N Taxilanes will be closed for 10-14 days between Taxilanes F and G during this phase as well. The vehicle service road (VSR) running east to west will be closed north of gates B12, B14, and B16, as well. A future notification will provide dates for this work.

The vehicle service road crossing of Ramp 2N and 2S closed north of Gate B22 (markings will be removed) during this phase.

During this time, the tunnel between Gates B22 and B24 will be closed.

The phase is currently scheduled to be completed by May 26th, 2023. Please see image of Phase 4 below:

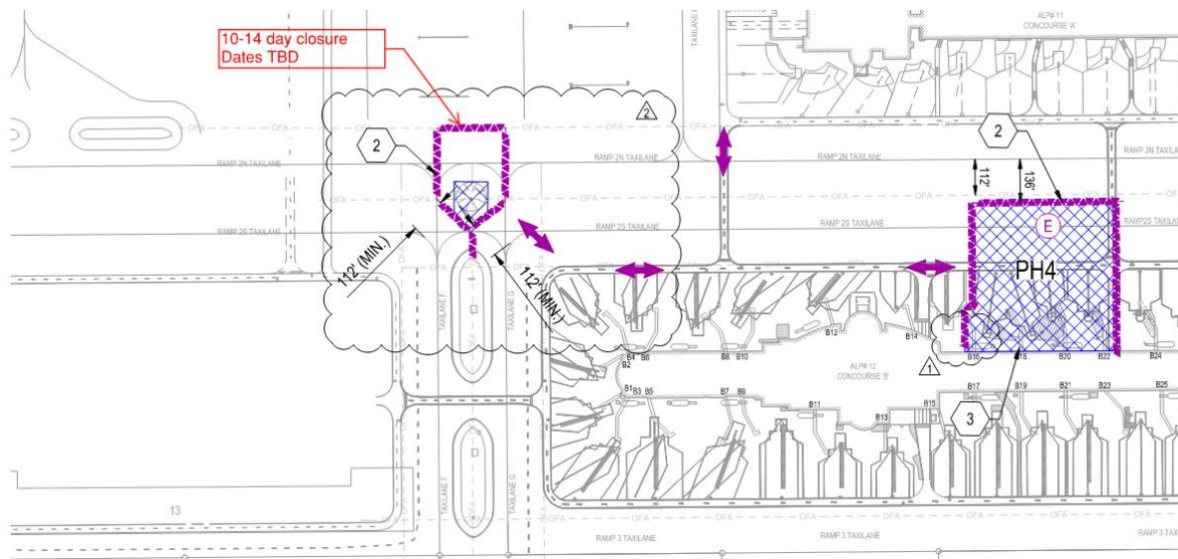

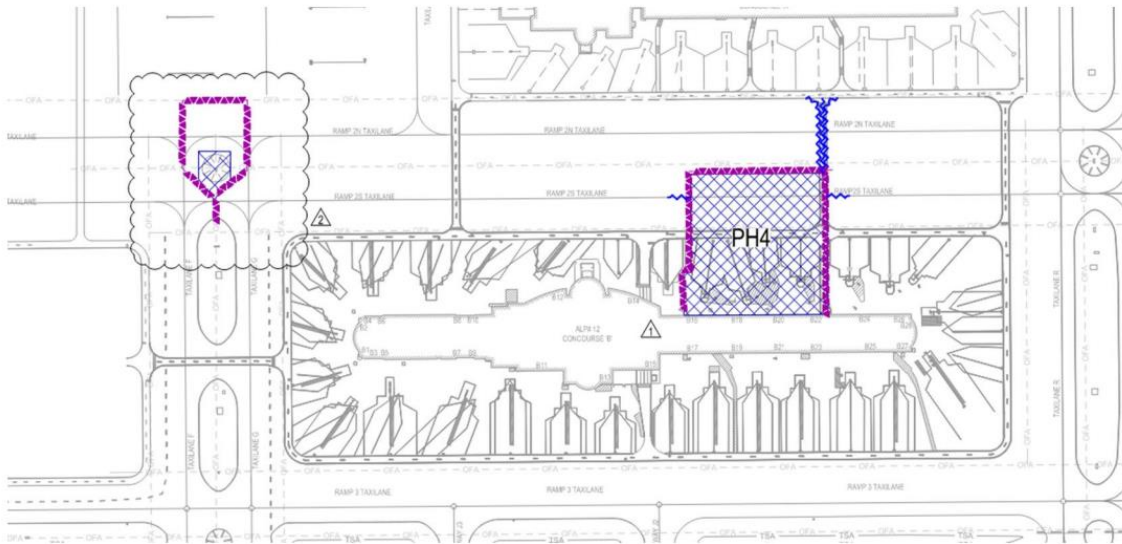


The work area will be surrounded by interlocking, low-profile barricades. ARFF routes will be provided with gaps in the barricade.

Pedestrians and vehicle traffic are to stay outside of the barricade during the closure. Additionally, you will find the most updated schedule based on the current timing of each phase below. ***Please note that the schedule is subject to change per delays that may occur during each phase.***

PHASE	START	FINISH	DAYS	GATE IMPACTS
7	10/03/22	11/15/22 Complete	43	B17, B19, B21 closed
6*	11/15/22	12/21/22 *Complete	45	B23, B25, B27 closed
2 Limited	01/03/23	01/31/23 Complete	29	B8, B10 available for RON
1 Limited	02/01/23	02/15/23 Complete	21	B8 closed; B4 & B6 open at night
2	02/20/23	03/31/23 Complete	40	B6, B8, B10 closed
3	03/31/23	04/27/23 (tentative)	26	B12, B14, B16 closed
4	04/28/23 (tentative)	05/26/23 (tentative)	31	B18, B20, B22 closed
5	05/27/23	07/01/23	36	B24, B26, B28 closed
1	07/02/23	08/04/23	34	B2, B4 closed
10	08/5/23	09/9/23	36	B1, B3 closed
9	09/10/23	10/13/23	34	B5, B7, B9 closed
8	10/15/23	11/11/23	29	B11, B13, B15 closed

*Some Phase 6 work postponed until 2023

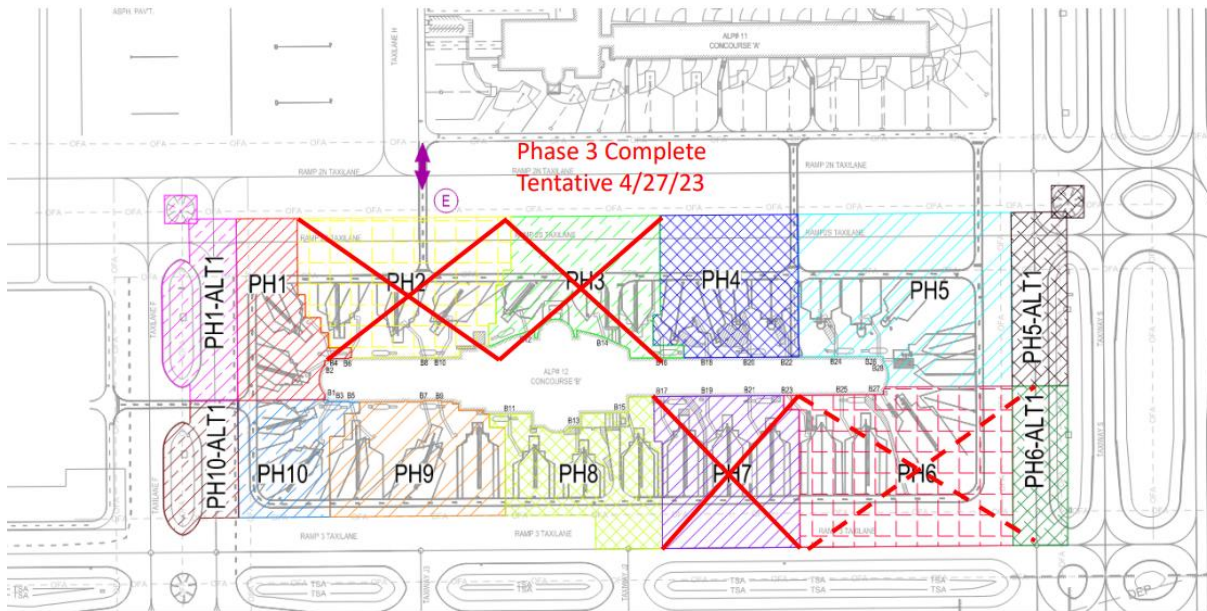

For questions regarding the project, please see the following contacts:

Damian Weller (CVG Airport Authority) – 859-206-2044 or dweller@cvgairport.com

JW Lucas (CVG Airport Authority) – 859-743-5861 or jucas@cvgairport.com
