

**To: CVG Airlines and Tenants**

**Subject: Concourse B Apron Rehabilitation Project Phase 1**

**Date: 07/03/2023**

## Effective July 10<sup>th</sup>, 2023

Beginning Monday, July 10th, weather pending, Harper Company will close out Phase 5 of Concourse B Apron Rehabilitation Project, and transition into Phase 1. **This will close Gates B2 and B4 after the early morning hours, followed by a reopening of Gates B24, B26, and B28 in the afternoon.**


Ramp 2S Taxilane will be closed at Taxilanes F and G north of Gate B4 for the duration of this phase. Taxilane F will be closed north of Gate B1. Taxilane G will be closed north of Gate B1.

The vehicle service road will be closed around Gates B2 and B4. The vehicle service road will also be closed crossing Taxilane G and F to Pad 13.

Additionally, please be aware that Gate B26 & B18 will close for the next Passenger Boarding Bridge Replacements on July 10.

The phase is currently scheduled to be completed on August 7<sup>th</sup>, 2023.

Please see images below:

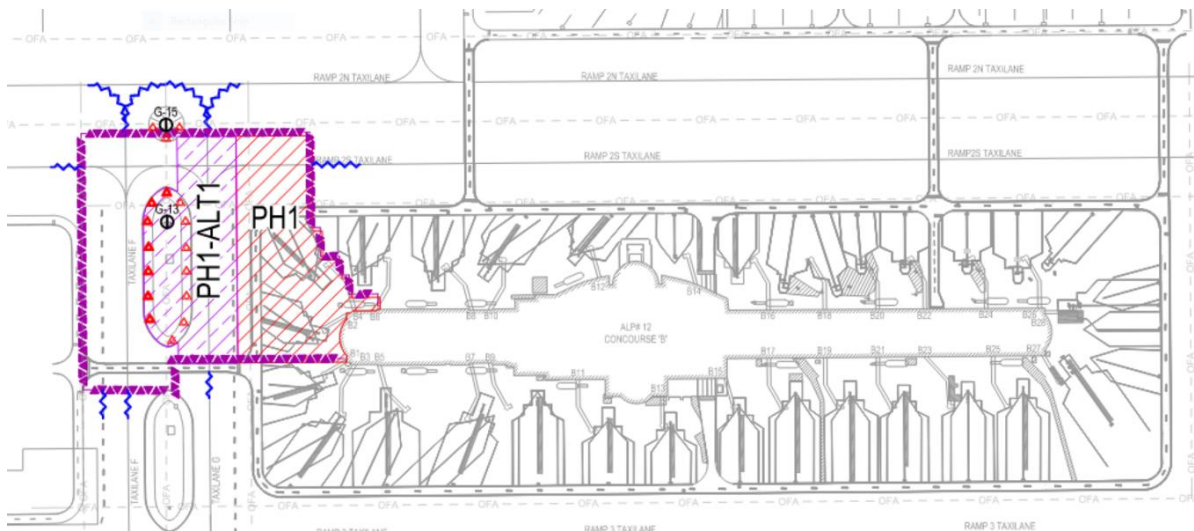


The work area will be surrounded by interlocking, low-profile barricades. ARFF routes will be provided with gaps in the barricade.

Pedestrians and vehicle traffic are to stay outside of the barricade during the closure.

Additionally, you will find the most updated schedule based on the current timing of each phase below. **Please note that the schedule is subject to change per delays that may occur during each phase.**

PHASE	START	FINISH	DAYS	GATE IMPACTS
7	10/03/22	11/15/22 Complete	43	B17, B19, B21 closed
6*	11/15/22	12/21/22 *Complete	45	B23, B25, B27 closed
2 Limited	01/03/23	01/31/23 Complete	29	B8, B10 available for RON
1 Limited	02/01/23	02/15/23 Complete	21	B8 closed; B4 & B6 open at night
2	02/20/23	03/31/23 Complete	40	B6, B8, B10 closed
3	03/31/23	04/27/23 Complete	26	B12, B14, B16 closed
4**	04/28/23	05/30/23 Complete	31	B18, B20, B22 closed
5	05/30/23	07/7/23 (tentative)	39	B24, B26, B28 closed
1	07/7/23 (tentative)	08/7/23 (tentative)	34	B2, B4 closed
10	08/8/23	09/13/23	36	B1, B3 closed
9	09/14/23	10/17/23	34	B5, B7, B9 closed
8	10/18/23	11/15/23	29	B11, B13, B15 closed

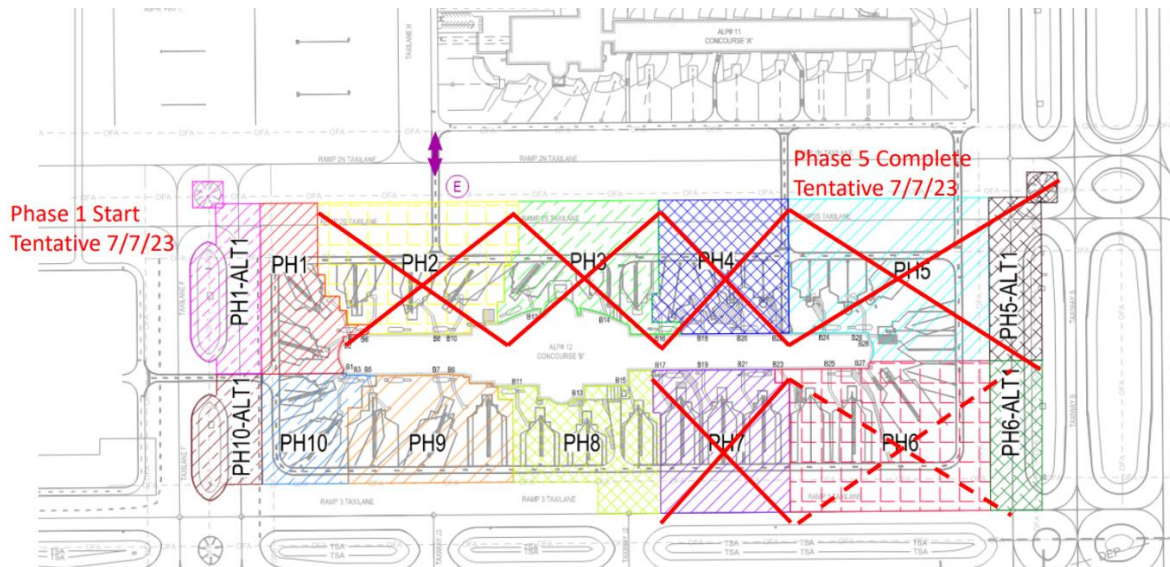

For questions regarding the project, please see the following contacts:

Damian Weller (CVG Airport Authority) – 859-206-2044 or [dweller@cvgairport.com](mailto:dweller@cvgairport.com)

JW Lucas (CVG Airport Authority) – 859-743-5861 or [jucas@cvgairport.com](mailto:jucas@cvgairport.com)
