

To: CVG Airlines and Tenants

Subject: Concourse B Apron Rehabilitation Project Phase 10

Date: 8/4/2023

Effective August 7th, 2023


Beginning Monday, August 7th, weather pending, Harper Company will close out Phase 1 of Concourse B Apron Rehabilitation Project, and transition into Phase 10.

This will close Gates B1 and B3 in the morning hours, followed by a reopening of Gates B2 and B4 in the afternoon. Additionally, please be aware that Gates B7 and B15 will be closed for bridge replacement starting August 7th through August 30th as scheduled, as well.

Ramp 3 will be closed between Taxiways E and G for the duration of this phase. Taxiway F will be closed north of Taxiway J to Taxiway 2S. Taxiway G will be closed north of Ramp 3 to Gate B2, B2 will be open. Spot 9 will be open, spot 10 is anticipated to be closed.

The vehicle service road will be closed around Gates B1 and B3. The vehicle service road will also be closed crossing Taxiways G and F to Pad 13.

The phase is currently scheduled to be completed on September 12th, 2023. Please see images below:

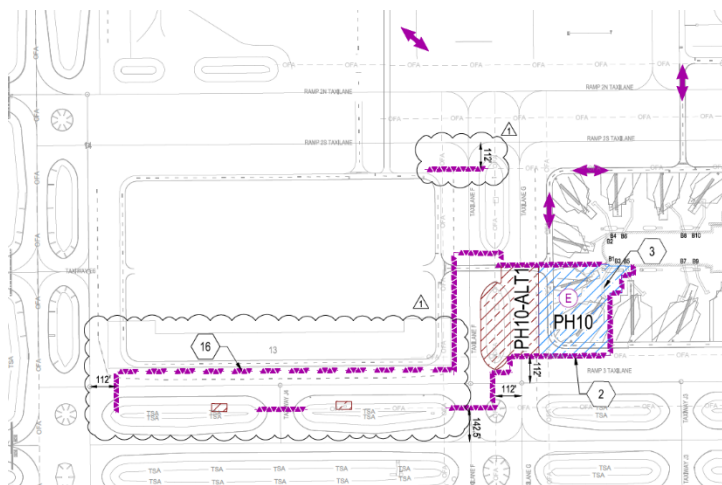


The work area will be surrounded by interlocking, low-profile barricades. ARFF routes will be provided with gaps in the barricade. Pedestrians and vehicle traffic are to stay outside of the barricade during the closure.

Additionally, you will find the most updated schedule based on the current timing of each phase below. ***Please note that the schedule is subject to change per delays that may occur during each phase.***

PHASE	START	FINISH	DAYS	GATE IMPACTS
7	10/03/22	11/15/22 Complete	43	B17, B19, B21 closed
6*	11/15/22	12/21/22 *Complete	45	B23, B25, B27 closed
2 Limited	01/03/23	01/31/23 Complete	29	B8, B10 available for RON
1 Limited	02/01/23	02/15/23 Complete	21	B8 closed; B4 & B6 open at night
2	02/20/23	03/31/23 Complete	40	B6, B8, B10 closed
3	03/31/23	04/27/23 Complete	26	B12, B14, B16 closed
4**	04/28/23	05/30/23 Complete	31	B18, B20, B22 closed
5	05/30/23	07/10/23 Complete	39	B24, B26, B28 closed
1	07/10/23	08/7/23 (tentative)	34	B2, B4 closed
10	08/7/23 (tentative)	09/13/23	37	B1, B3 closed
9	09/13/23	10/16/23	34	B5, B7, B9 closed
8	10/17/23	11/15/23	29	B11, B13, B15 closed

*Some Phase 6 work (joint sealing, markings) will occur during other phases.
** Isolated concrete repair in Phase 4 and be complete.

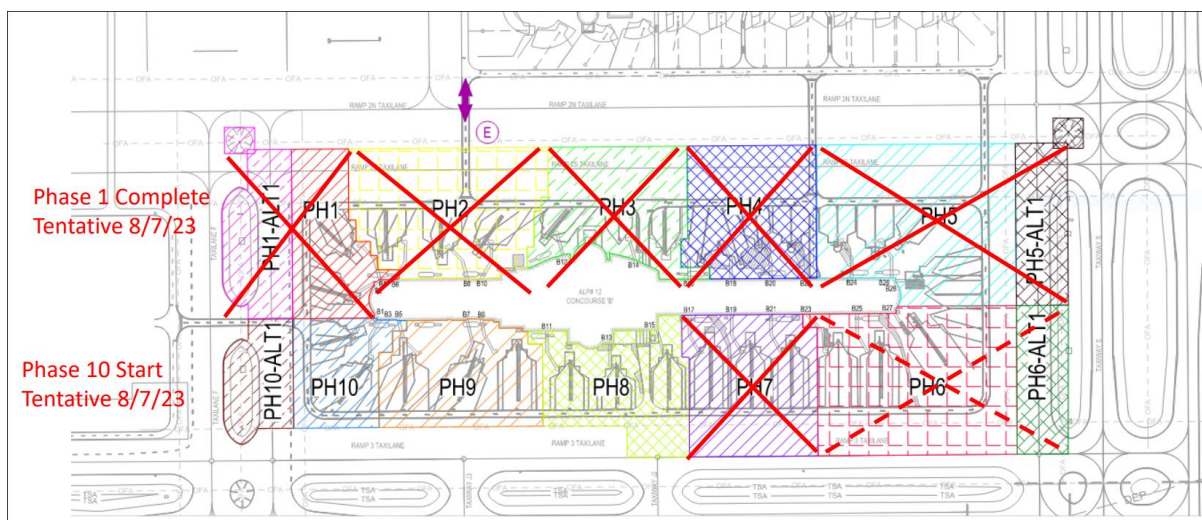

For questions regarding the project, please see the following contacts:

Damian Weller (CVG Airport Authority) – 859-206-2044 or dweller@cvgairport.com
JW Lucas (CVG Airport Authority) – 859-743-5861 or jlucas@cvgairport.com
