

To: CVG Airlines and Tenants
Subject: MULTIPLE PROJECTS NOTIFICATION
Date: 09/11/2023

Effective September 12th, 2023


Beginning Tuesday, September 12th, weather pending, Harper Company will close out Phase 10 of Concourse B Apron Rehabilitation Project, and transition into Phase 9.

This will close Gates B5, B7, and B9 in the morning hours, followed by a reopening of Gates B1 and B3 in the afternoon. Additionally, please be aware that Gates B17 and B19 will be closed for bridge replacement through September 27th as scheduled. This will also include a closure of B25 and B10 from October 2nd through October 25th. (These two scheduled replacements will conclude the first phase of the Passenger Boarding Bridge Replacement Project.)

Ramp 3 will remain open throughout the duration of this phase. Some daily closures will occur for limited work outside of the barricades.

The vehicle service road will be closed south of Gates B5, B7, and B9. Thus, access from the east or west will dead end at this location. Traversing south around the barricaded vehicle service road is not allowed.

This next upcoming phase [9] is currently scheduled to be completed on Friday, October 13th, 2023. Please see images below:

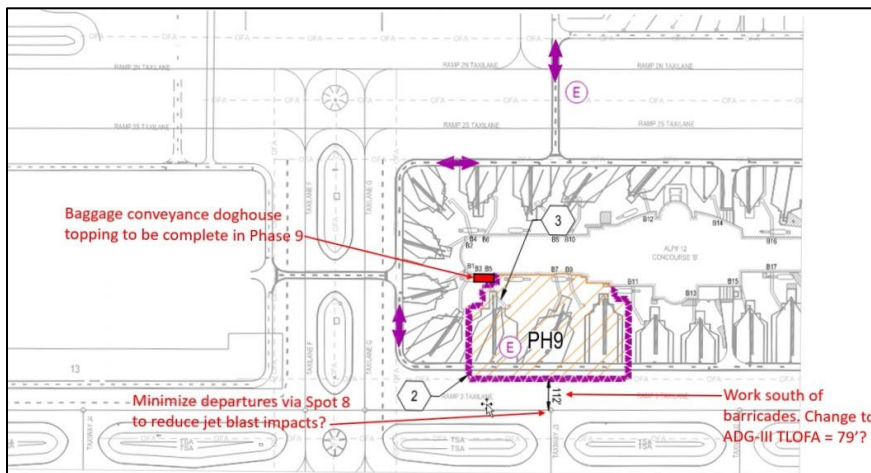


The work area will be surrounded by interlocking, low-profile barricades. ARFF routes will be provided with gaps in the barricade. Pedestrians and vehicle traffic are to stay outside of the barricade during the closure.

Additionally, you will find the most updated schedule based on the current timing of each phase below. **Please note that the schedule is subject to change per delays that may occur during each phase.**

PHASE	START	FINISH	DAYS	GATE IMPACTS
7	10/03/22	11/15/22 Complete	43	B17, B19, B21 closed
6*	11/15/22	12/21/22 *Complete	45	B23, B25, B27 closed
2 Limited	01/03/23	01/31/23 Complete	29	B8, B10 available for RON
1 Limited	02/01/23	02/15/23 Complete	21	B8 closed; B4 & B6 open at night
2***	02/20/23	03/31/23 Complete	40	B6, B8, B10 closed
3	03/31/23	04/27/23 Complete	26	B12, B14, B16 closed
4**	04/28/23	05/30/23 Complete	31	B18, B20, B22 closed
5	05/30/23	07/10/23 Complete	39	B24, B26, B28 closed
1	07/10/23	08/7/23 Complete	34	B2, B4 closed
10	08/7/23	09/11/23 (tentative)	37	B1, B3 closed
9	09/11/23 (tentative)	10/13/23	34	B5, B7, B9 closed
8	10/17/23	11/15/23	29	B11, B13, B15 closed

*Outstanding Phase 6 work (joint sealing, gate markings) at Gates B23, B25 & B27 to be complete (Fall 2023)
 ** Phase 4 isolated concrete repair in at Gate B20 to be complete (Fall 2023)
 *** Phase 2 Doghouse pavement repairs at Gates B6, B8 and B10 to be complete (Fall 2023)

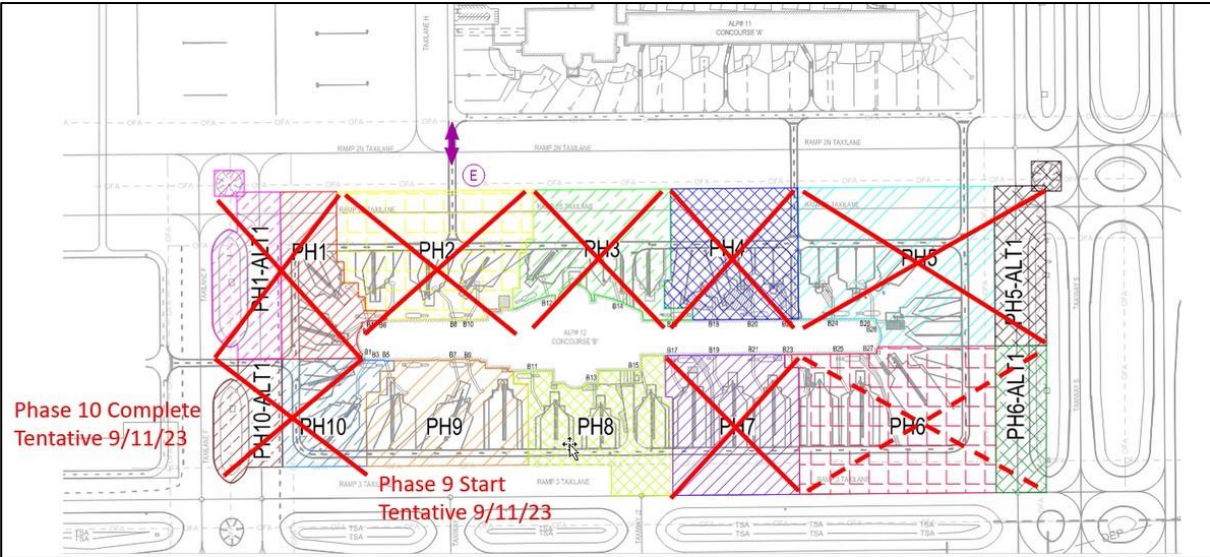

For questions regarding the project, please see the following contacts:

- Damian Weller (CVG Airport Authority) – 859-206-2044 or dweller@cvgairport.com
- JW Lucas (CVG Airport Authority) – 859-743-5861 or jlucas@cvgairport.com
